


Bond Program Project Schedules

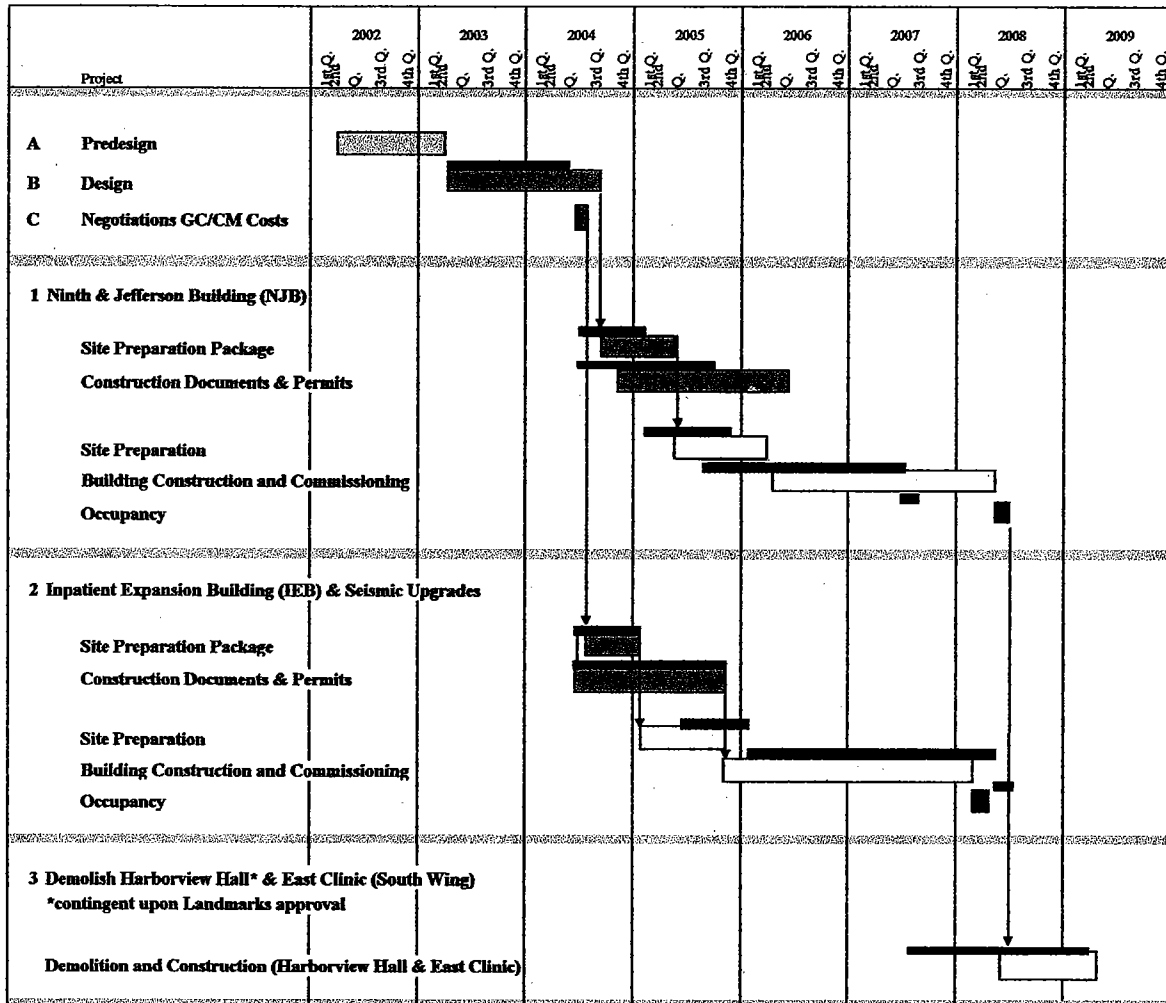

	ORIGINAL	NOW
▪ Predesign	Mar 2002 – Mar 2003	Mar 2002 – Mar 2003
▪ Design and Permitting	April 2003 – Oct 2005	April 2003 – June 2006
▪ Construction		
○ Ninth & Jefferson Building (NJB)	Jan 2005 – June 2007	May 2005 – May 2008
○ Inpatient Expansion Building (IEB) & Seismic Upgrade	June 2005 – April 2008	Jan 2005 – Feb 2008
○ Proposed Demolitions of Harborview Hall & East Clinic (South Wing) (Harborview Hall after Landmarks Review)	July 2007 – Mar 2009	June 2008 – April 2009
